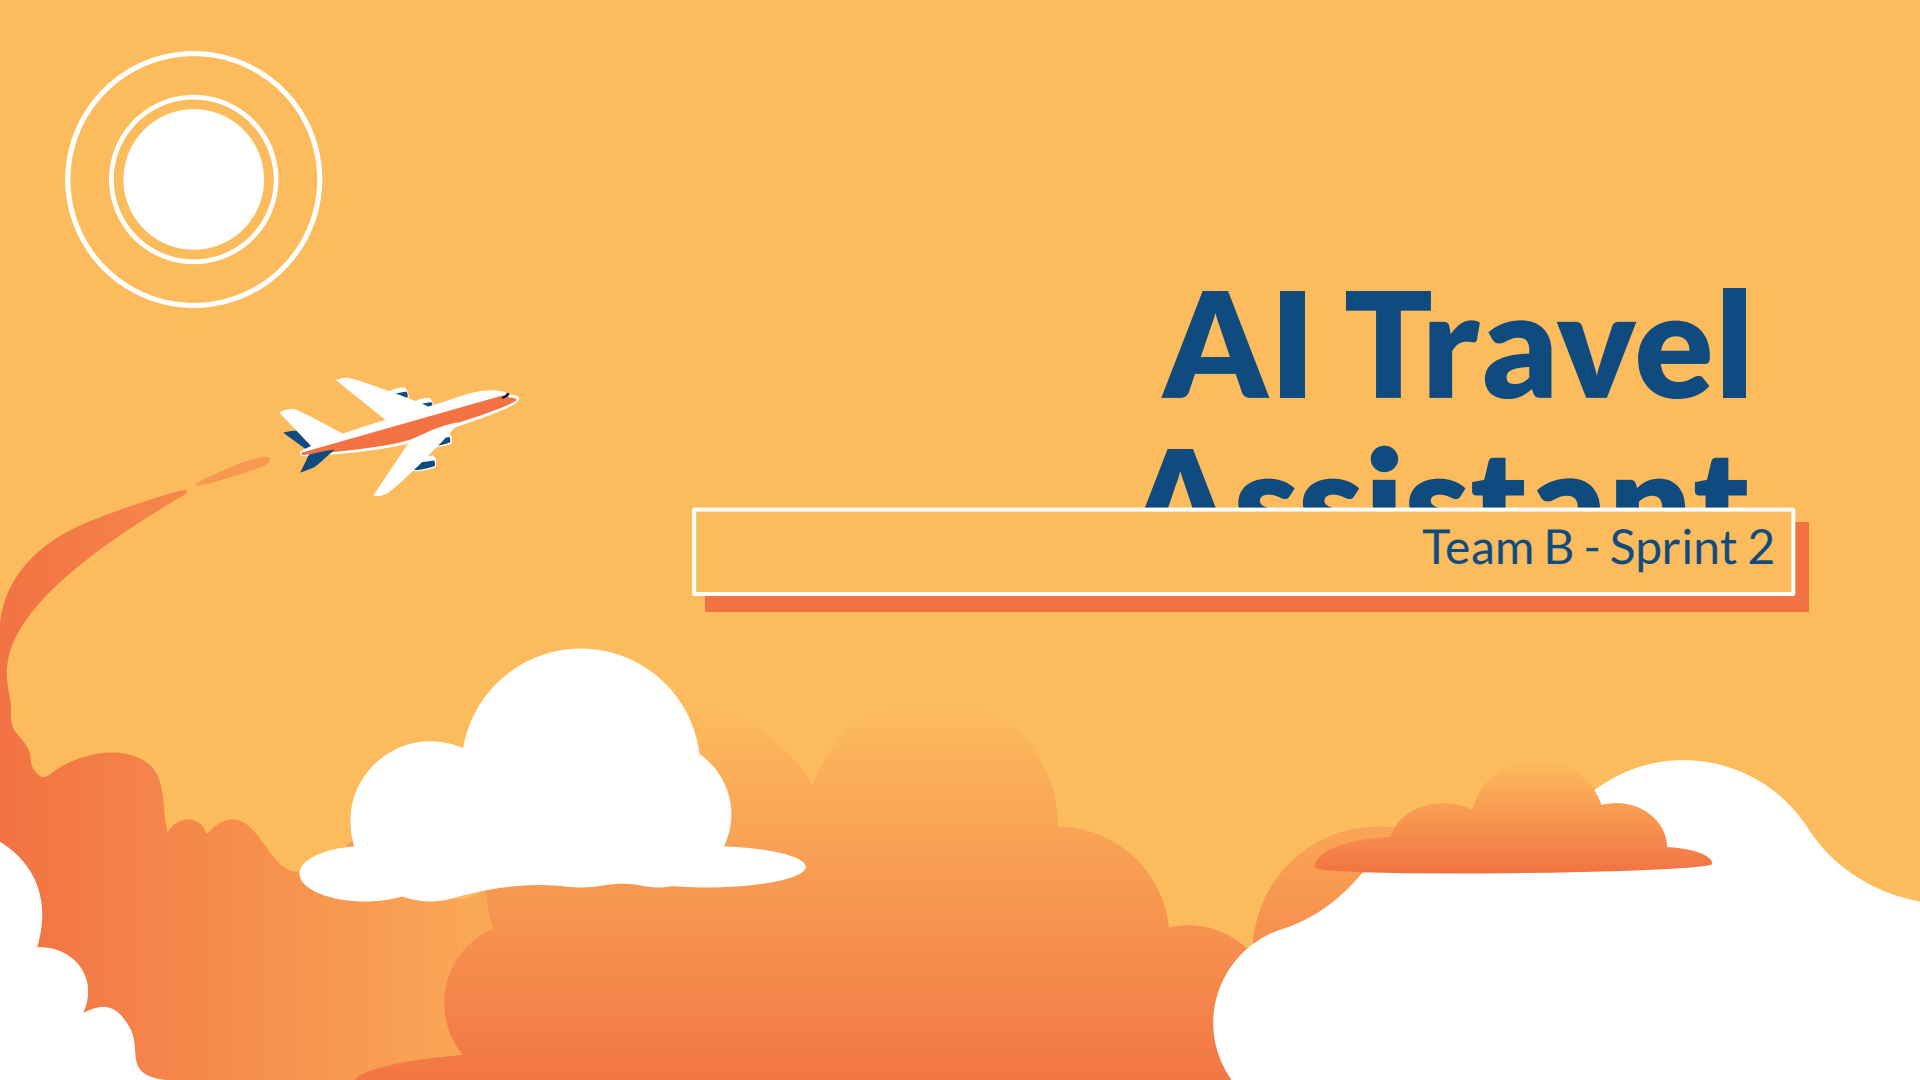


AI Travel Assistant

Team B - Sprint 2


Project Overview

Your Accessible Flight - Accessible Travel Assistance Chatbot

Problem: PRM users can struggle to find relevant accessibility and travel-assistance information.

Users: PRMs (Passengers with Reduced Mobility)

Goal: To improve YAF's existing chatbot so that PRM users can ask questions to the chatbot and receive information that assists them.

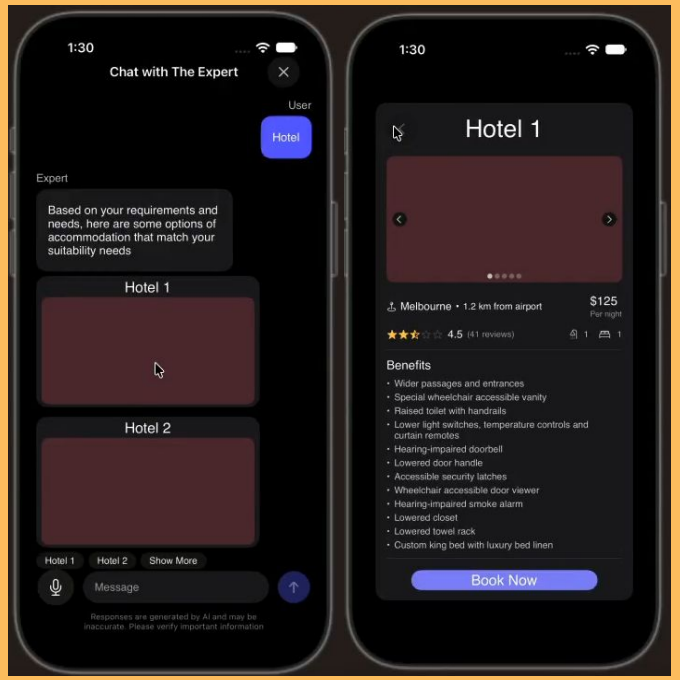

Original Plan


S2 commitment - Contingency prototype

- Functional chatbot interaction
- Backend retrieval using mock data
- Frontend chatbot interface
- Backend <-> Frontend integration
- Basic accessibility/usability validation

Actual Achievement

Walkthrough video of current application built by Team B ->

- Currently responds based on keywords from user input.
- Placeholder images will be replaced with proper Hotel photos later on.
- Ideally in Sprint 3, we can display hotel data from the external database instead of mock data.

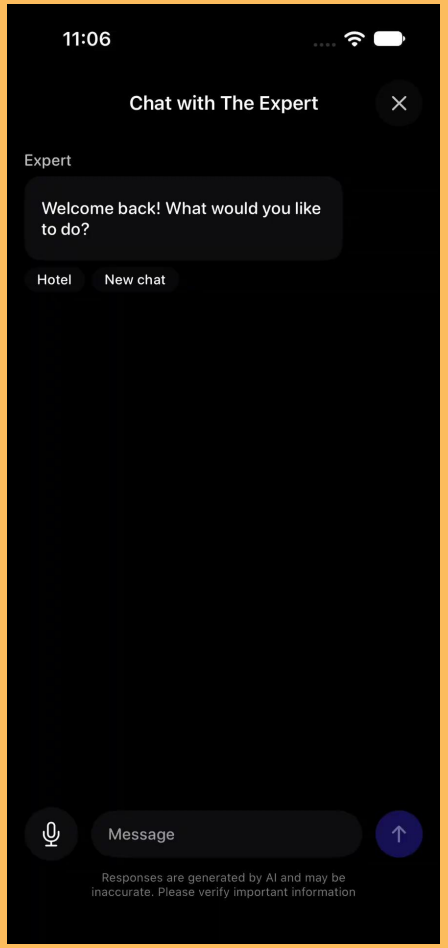

Why It Matters

For a user:
A more direct way to access travel assistance information.

- Users can interact with the chatbot directly through the interface rather than with backend functionality separately.
- User input can be used to identify relevant information and return an appropriate response.
- Supporting information such as hotel cards can be presented to inform the user.

For the client:
Demonstrates the direction of the enhanced chatbot.

- Provides a working prototype of how chatbot responses and supporting information can be presented to users.
- Demonstrates current chatbot can be extended into a more interactive experience for users.
- Establishes a foundation that could be taken on in the future to adapt to real data and resources.

Blockers/Open Questions

Blockers:

- Team B is still on hold for the receival of the external Hotel.eu database.

Open questions:

- Localisation specification, such as which language(s) to prioritise first if we were to move in that direction for Sprint 3.

Task Allocation & Time Spent

Member:	Task(s):	Hours:
PM - Johanne Gutierrez	3	8 (480mins)
Dev - Sean Mojica	3	12 (720mins)
Dev - Nguyen Phuong	3	12 (720mins)
BA - Ethan Dalianis	4	12 (720mins)
UX - Rajvansh Padda	4	12 (720mins)

Timeline & Next Steps

Timeline:

Client meeting with YAF: 15/09, (We've attempted to schedule a meeting for 2/10, however a lack of response made this unable to happen, we will send a message detailing what's happened over the Sprint to inform them)

Internal meetings: 16/09, 23/09, 30/09

Supervisor meetings:
Tech w/ Naresh - 21/09
Non-tech with Leon - 24/09


Next steps:

Await external database from Hotel.eu

If we aren't able to receive the database, we will continue to work on the prototype that Team 36 has created and continue to improve upon it, making it more complete and presentable.


Rajvansh Singh Padda - UX + DEV

Week 1 : Reviewed Wireframes and created dev documation
Week 2 : Completed core application in swift
Week 3 : Completed Prototype and Prepared for Integration

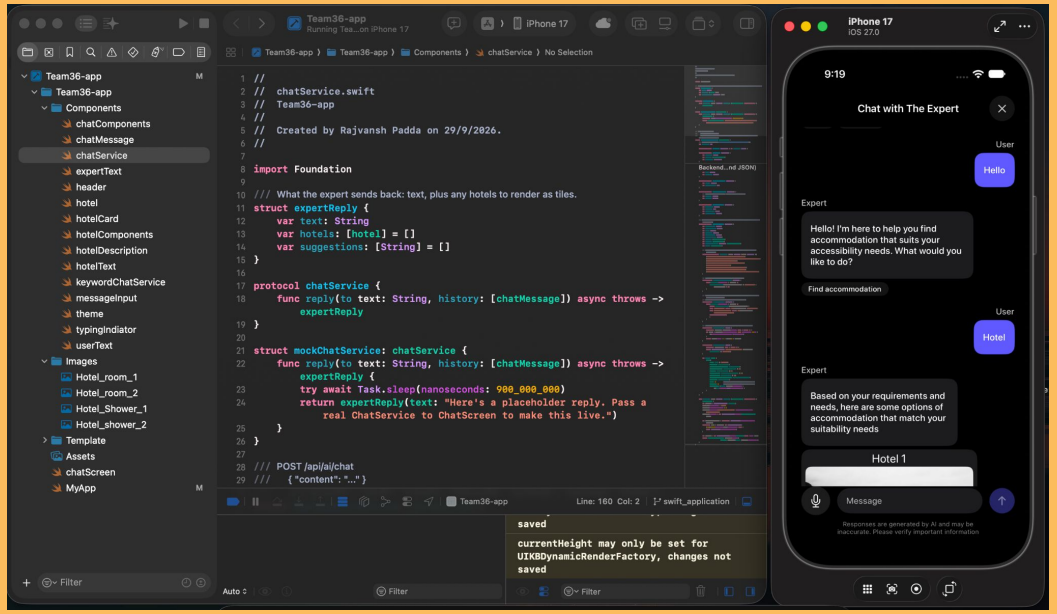

Sean Renzo Mojica (Dev)

Week 1: Establish AI provider connection for the chatbot
Week 2: Implement prototype chatbot data retrieval
Week 3: Connect SwiftUI to chatbot endpoint

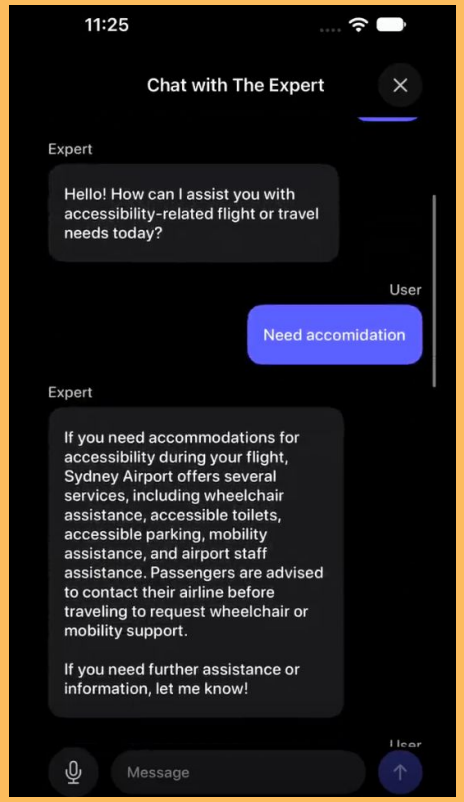

Nguyen Phuong Vo (Dev)


- Week 1: Built a provider-neutral hotel schema and synthetic dataset
- Week 2: Expanded the dataset
- Week 3: Improved how the chatbot uses hotel data in responses


```
{
  "provider": "yaf-local-fixture",
  "providerId": "SYD-H003",
  "airportIata": "SYD",
  "name": "Harbour Inclusive Suites",
  "address": "80 C Avenue, Sydney NSW",
  "distanceKm": 6.8,
  "description": "Suite accommodation with several confirmed accessibility features.",
  "images": [{"url": "https://example.test/images/SYD-H003-room.jpg", "altText": "Fictional inclusive hotel suite"}],
  "rating": {"score": 4.7, "reviewCount": 41},
  "accessibility": {
    "stepFreeEntrance": {"status": "confirmed", "source": "fictional fixture"},
    "wheelchairAccessibleRoom": {"status": "confirmed", "source": "fictional fixture"},
    "rollInShower": {"status": "confirmed", "source": "fictional fixture"},
    "accessibleParking": {"status": "unknown", "source": "not supplied"},
    "accessibleAirportShuttle": {"status": "unknown", "source": "not supplied"},
    "accessibleToilet": {"status": "confirmed", "source": "fictional fixture"},
    "grabRails": {"status": "confirmed", "source": "fictional fixture"},
    "emergencyCallCord": {"status": "provider_claimed", "source": "fictional fixture"}
  },
  "offer": {"currency": "AUD", "nightly": 225, "available": false, "bookingUrl": "https://example.test/hotels/SYD-H003"},
  "sourceUrl": "https://example.test/hotels/SYD-H003",
  "retrievedAt": "2026-09-16T09:00:00+10:00"
}
```


```
welcome@DESKTOP-SPBG9GB MINGW64 ~/Documents/GitHub/yaf-backend (feature/team-b-ai-retrieval-prototype)
$ go run ./cmd/api
2026/10/02 10:17:19 airport provider: airlabs (RMO/KIV via airport.md)
2026/10/02 10:17:19 ai provider: pinecone
2026/10/02 10:17:19 ai provider: mock
2026/10/02 10:17:19 AUTH_ENABLED=false running with dev auth, do not use in production
2026/10/02 10:17:19 Server running on :8080
```

Ethan Dalianis (BA)

- Week 1: Task 3: Review and refined Sprint 2 functional requirements. Task 4: Defined minimum hotel/booking information.
- Week 2: Task 5: Validated accessibility and usability of the chatbot thus far.
- Week 3: Task 6 Conducted final Sprint 2 end to end testing.



Successful – tested in the prototype

- Input: "I use a manual wheelchair I need step free access in my hotels" (free text), then the "Wider entrances" quick-reply chip when the system asked about further needs.
- Expected: Needs are captured without the system assuming anything further.
- Result: Pass
- Notes: The system captured the free-text need, asked for a clarifying follow-up through quick-reply to chips rather than assuming extra needs (e.g. didn't assume wider entrances were needed), and confirmed the combined needs back before asking for destination and dates. Meets US-1's requirement to communicate needs via free text or guided prompts with no assumptions.
