

01 Project Overview

Current system:

Travel accessibility application featuring airport and airline information with a chatbot help functionality.

What we're improving:

The AI Chatbot functionality in the application to give better and more detailed answers to users.

Who is the target audience of the app?

PRMs
(Passengers with reduced mobility)

What is the intended improved experience?

ChatGPT-like text response with supporting links/picture/information below the text response + service integration

02 Original Sprint 1 Plan: What we planned to deliver

Week 1:	Week 2:	Week 3:
Project repository and development environment setup	Client requirements clarification and prioritisation	Finalise MVP requirements and acceptance criteria
Establish application architecture and technology stack	Accessible traveller user journey analysis	Create accessible interface wireframes
Initial client requirements analysis	AI and third-party service research	Finalise API and data requirements
User needs and accessibility research	Initial travel assistant user flow	Sprint 1 review and client alignment
Project documentation and requirements coordination	Technical feasibility review	Finalise technical architecture and development environment


03

Actual Achievement: What we actually delivered - Part 1

Week 1:	Week 2:	Week 3:
Set up shared development environment	Review technical feasibility and constraints	Identify and prepare the development environment for Sprint 2 implementation
Research user needs and accessibility considerations	Create initial chatbot interaction wireframe	Refine chatbot interface design and accessibility features
Define technical architecture and technology stack	Reviewing existing chatbot implementation	Define sprint 2 technical implementation approach.
Analyse initial client requirements	Define MVP requirements and acceptance criteria	Establish possible user stories for chatbot testing
Create meeting template	Develop user interaction flow for the improved chatbot	Coordinate Sprint 1 findings and coordinate playback preparations
Coordinate Sprint 1 requirements and documentation		

03 Actual Achievement: What we actually delivered - Part 2

Team environment in client repository

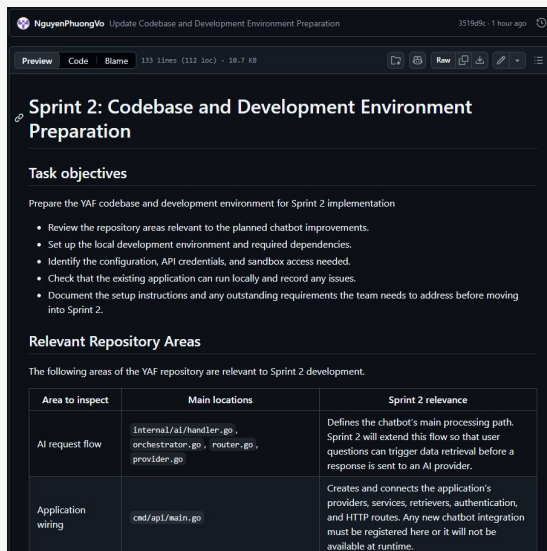

The screenshot shows a GitHub repository page for 'Sprint 2: Codebase and Development Environment Preparation' by user 'NguyenPhuongVo'. The page includes a 'Preview' tab, a 'Code' tab, and a 'Blame' tab. The 'Code' tab is selected, showing the repository's file structure and a table of relevant repository areas.

Sprint 2: Codebase and Development Environment Preparation

Task objectives

Prepare the YAF codebase and development environment for Sprint 2 implementation


- Review the repository areas relevant to the planned chatbot improvements.
- Set up the local development environment and required dependencies.
- Identify the configuration, API credentials, and sandbox access needed.
- Check that the existing application can run locally and record any issues.
- Document the setup instructions and any outstanding requirements the team needs to address before moving into Sprint 2.

Relevant Repository Areas

The following areas of the YAF repository are relevant to Sprint 2 development.

Area to inspect	Main locations	Sprint 2 relevance
AI request flow	<code>internal/ai/handler.go</code> , <code>orchestrator.go</code> , <code>router.go</code> , <code>provider.go</code>	Defines the chatbot's main processing path. Sprint 2 will extend this flow so that user questions can trigger data retrieval before a response is sent to an AI provider.
Application wiring	<code>cmd/api/main.go</code>	Creates and connects the application's providers, services, retrievers, authentication, and HTTP routes. Any new chatbot integration must be registered here or it will not be available at runtime.

User stories to test chatbot against

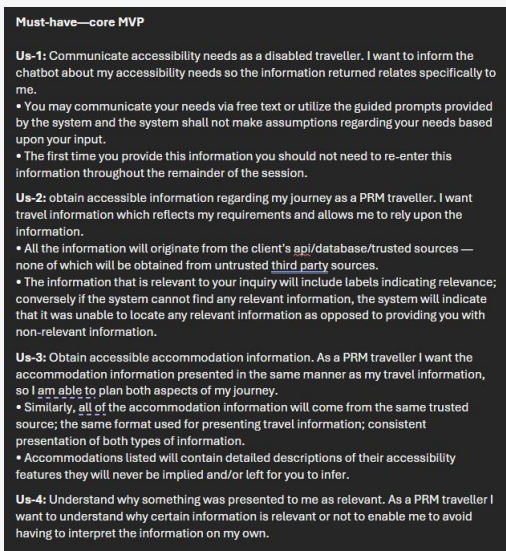

The screenshot shows a document titled 'Must-have—core MVP' with four user stories (Us-1 to Us-4) for a chatbot. The stories are written from the perspective of a PRM traveller and focus on accessibility needs and accommodation information.

Must-have—core MVP

Us-1: Communicate accessibility needs as a disabled traveller. I want to inform the chatbot about my accessibility needs so the information returned relates specifically to me.

- You may communicate your needs via free text or utilize the guided prompts provided by the system and the system shall not make assumptions regarding your needs based upon your input.
- The first time you provide this information you should not need to re-enter this information throughout the remainder of the session.

Us-2: obtain accessible information regarding my journey as a PRM traveller. I want travel information which reflects my requirements and allows me to rely upon the information.


- All the information will originate from the client's api/database/trusted sources—none of which will be obtained from untrusted third party sources.
- The information that is relevant to your inquiry will include labels indicating relevance; conversely if the system cannot find any relevant information, the system will indicate that it was unable to locate any relevant information as opposed to providing you with non-relevant information.

Us-3: Obtain accessible accommodation information. As a PRM traveller I want the accommodation information presented in the same manner as my travel information, so I am able to plan both aspects of my journey.

- Similarly, all of the accommodation information will come from the same trusted source; the same format used for presenting travel information; consistent presentation of both types of information.
- Accommodations listed will contain detailed descriptions of their accessibility features they will never be implied and/or left for you to infer.

Us-4: Understand why something was presented to me as relevant. As a PRM traveller I want to understand why certain information is relevant or not to enable me to avoid having to interpret the information on my own.

Example Figma frames depicting chatbot interaction

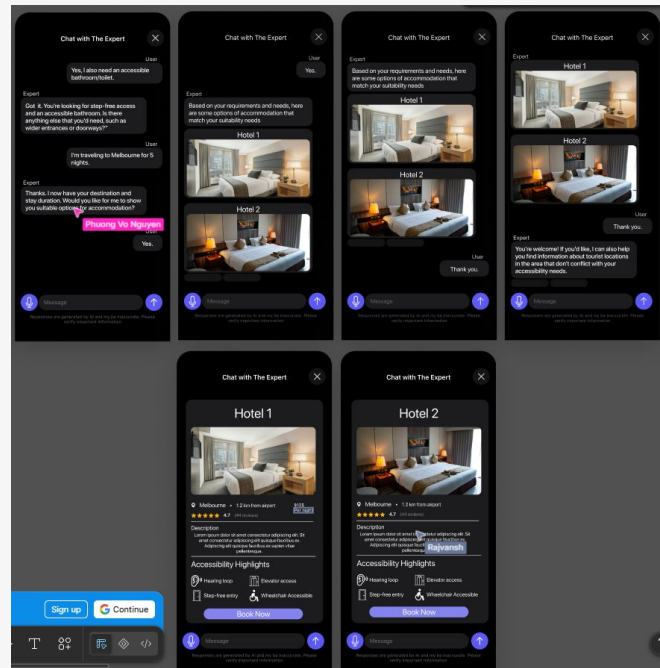

The screenshot shows a series of Figma frames depicting chatbot interactions for a travel application. The frames are arranged in a grid, showing the chatbot's response to user queries and the user's input.

The frames show the chatbot's response to user queries and the user's input. The chatbot's response includes a list of hotels with images and details, and the user's input includes a 'Book Now' button.

The frames show the chatbot's response to user queries and the user's input. The chatbot's response includes a list of hotels with images and details, and the user's input includes a 'Book Now' button.

04 Why It Matters

For the user:

- More accessible interaction
- Clearer information
- More personalised assistance

For the client:

- Improves existing functionality
- Better support for their users
- Clearer path to implementation

For the project:

- Clearer foundation for development
- Reduction of uncertainty before development
- Priorities established for Sprint 2

05 Blockers & Open Questions

Hotel/Booking database:

Awaiting information - Team has identified this as important information to gather before starting Sprint 2.

We will inquire about this during our client meeting tomorrow.

Chat history retention:

Should chatbot conversations be stored? Or should they be temporary only?

We will also inquire about this during the client meeting tomorrow.

06 Task Allocation & Time Spent

Member:	Task(s):	Hours:
PM - Johanne Gutierrez	3	9 (540min)
Dev - Sean Mojica	3	10 (600min)
Dev - Nguyen Phuong	3	10 (600min)
BA - Ethan Dalianis	4	13 (720min)
UX - Rajvansh Padda	3	9 (540min)

07 Timeline & Next Steps

Timeline:

Client meetings with YAF: 07/08, 14/08, 21/08, 11/09 - Fridays

Internal meetings: 05/08, 12/08, 19/08, 26/08, 09/09 - Every Wednesday

Supervisor meetings:

Tech w/Naresh - 17/08

Non-tech w/Leon - 27/08

Playback - 10/09

What's happening next sprint:

Improvement of the chatbot functionality:

- Text response with detailed information pertaining to user needs
- Supporting information/links/pictures to give the user more to work with

Ethan Dalianis (BA)

Sprint 1 Weeks 1 & 2:

- Reviewed and confirmed client requirements.
- Defined the core problem: Improving accessibility for travel for disabled users.
- Agreed on 10 functional requirements and 6 design requirements for the development team to utilise
- Locked in technical restraints: Using the clients AI API and trusted database only.

Ethan Dalianis (BA)



Sprint 1 Week 3

- Refined the MVP requirements into 12 prioritised user stories.
- Clear acceptance criteria in the user stories.
- Prioritised the user stories using MoSCoW style must have 6, Should have 2 and 4 could have.



Sprint 1: Week 1,2 & 3

- Researched user needs and requirements for Persons with accessibility needs
- Created Base Wireframes
- Refined Wireframes according to changes
- Created and documented Refined designs for chat bot
- Created Working Prototype for Chat bot

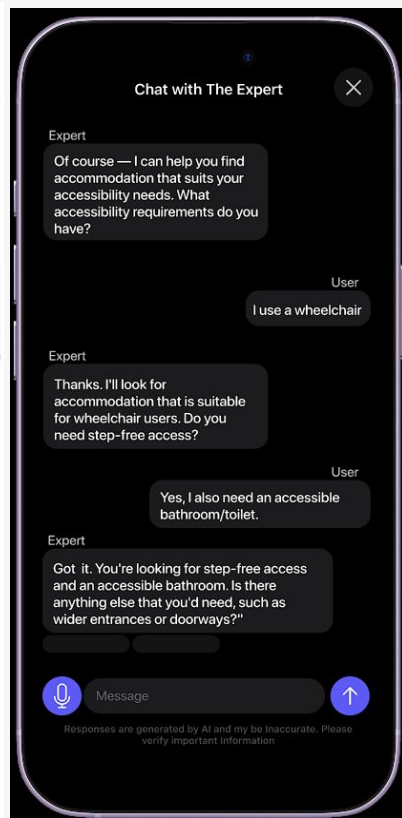



Figma Design

- Completed Figma Design

Prototypes


- Dark Mode
- Light mode



Nguyen Phuong Vo (Dev)

Sprint 1: Week 1 & 2

- Set up repository and documented requirements
- Reviewed YAF backend
- Refined requirements and user flow
- Identified technical risks and dependencies

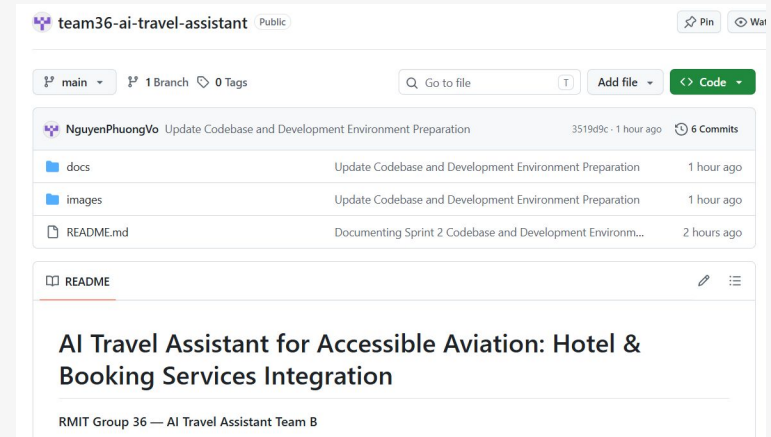

Nguyen Phuong Vo (Dev)

Sprint 1: Week 3

- Reviewed key YAF backend and AI components for Sprint 2
- Verified dependencies and successfully ran the backend
- Created the Team B integration branch
- Documented remaining dependencies and confirmed local codebase readiness

Sean Renzo Mojica(Dev)

Sprint 1: Week 1 - 3

- Set up document for technical architecture and technology stack
 - frontend using react and next.js with backend using node.js
- Set up document for reviewing existing chatbot implementation
 - Multiple AI providers and PostgreSQL database
- Set up document for Sprint 2 technical implementation approach
 - client-provided hotel or booking API
- These documents are put in the github repository
